CIVIL-TECH CONSULTANTS AND ENGINEERS

Building & Highway Material Testing Laboratory

An ISO 9001:2015 Certified Company

NABL - Accredited Laboratory as per ISO / IEC-17025 : 2005

JAS-ANZ BSCIC ISO 9001 REGISTERED

No. : CTCE/BBMP/PMC/B-D/2019-20/100

Date: 31.08.2019

To,

Executive Engineer,

Byatarayanapura Division,

Bruhat Bangalore Mahanagara Palike,

Bangalore.

CERTIFICATE

Reference : BBMP/EE/BTP/WO/233/2018-19 Date: 26.02.2019

Name of work: Improvements to Drains at Syndicate Bank road 5th Block BEL Layout in Ward No.09 (Vidyaranyapura), Vidyaranyapura Sub Division, BBMP, Bangalore. This is to certified that the 1st and Final bill of the above said work has been executed satisfactorily and the quantities of work done has also been certified.

Thanking you,

With Regards,

For Civil-Tech Consultants and Engineers

31/8/2019

Authorized Signature

AE-9

Assistant Executive Engineer
Vidyaranyapura Sub Division
BBMP, Bangalore - 97

#23/14, 7th Cross, 3rd Stage, 4th Block, Shakthi Ganapathi Nagara, Basaveshwaranagara, Bangalore-79.

Tele fax : 23223227, Cell : 93428 39190, Website : www.civiltechconsultants.com

e-mail : vishwanath.ia@civiltechconsultants.com / info@civiltechconsultants.com

CIVIL-TECH CONSULTANTS AND ENGINEERS

Building & Highway Material Testing Laboratory

An ISO 9001:2015 Certified Company

NABL - Accredited Laboratory as per ISO / IEC-17025 : 2005

JAS-ANZ BSCIC ISO 9001 REGISTERED

No. : CTCE/BBMP/PMC/B-D/2019-20/100

Date: 31.08.2019

To,

Executive Engineer,

Byatarayanapura Division,

Bruhat Bangalore Mahanagara Palike

Bangalore.

COMPLIANCE REPORT

Dear Sir,

Reference : BBMP/EE/BTP/WO/233/2018-19 Date: 26.02.2019

Name of work: "Consultancy services for Construction Supervision, Project Management and quality assurance for the works in ward No. 09, 10 and 11 (Number of works-33)"

Sub Name of Work: Improvements to Drains at Syndicate Bank road 5th Block BEL Layout in Ward No.09 (Vidyaranyapura), Vidyaranyapura Sub Division, BBMP, Bangalore.

With respect to the above subject & name of the work, we have supervised the work and the quantity and quality of below mentioned items of the work was found to be completed satisfactorily for the **1st and Final bill**

Sl. No	Description of Work	Unit	Qty
1	KSRRB 300- 1. Earthwork excavation by manual means in ordinary soil involving an average horizontal trrow upto 2 meters and an average lift upto 0.5m, excavated surface leveled and sides neatly dressed, the disposed earth to be leveled neatly after breaking of clods complete as per specifications. MORTH / Chapter 3 Page No.143 / Item No. 19.1, PWD SR 2018-19	Cum	147.02
2	Removing and refixing stone slabs of drains and pointing in CM (1:3) etc., complete as per the direction of engineer incharge	Sqm	724.95
3	Providing granite slabs of selected quality roughly dressed having a aize of 7.5 cms thick and fixed in cement mortor (1:6) including fixing curing etc., complete Page No.27 / Item No. 5.31 PWD SR 2018-19	Sqm	87.75
4	KSRB 5-14 : Providing and constructing load bearing wall with solid concrete blocks of size 400x150x200 mm having block density not lessthan 1800 kg/m3 and having a minimum average compressive strength 4.00 N/mm2 confirming to IS 2185 (Part) : 2005 and constructed with CM 1:4, as per IS 2572:2005 including cost of all materials, labour charges, scaffolding, curing complete as per specifications. KSB No. 5.4 Page No. 27 / Item No. 5.26.2, PWD SR 2018-19	Sqm	580.80

Assistant Executive Engineer
Vidyaranyapura Sub Division
BBMP, Bangalore - 97

Civil-Tech Consultants & Engineers Bangalore

#23/14, 7th Cross, 3rd Stage, 4th Block, Shakthi Ganapathi Nagara, Basaveshwaranagara, Bangalore-79.

Tele fax : 23223227, Cell : 93428 39190, Website : www.civiltechconsultants.com

e-mail : vishwanath.ia@civiltechconsultants.com / info@civiltechconsultants.com

Sl. No	Description of Work	Unit	Qty
5	KSRB 4-1.6 : Providing and laying ia position plain cement concrete of mix 1:2:4 with cement @ 240kgs, with 20mm and down size graded granite metal coarse aggregates @ 0.69 cum and fine aggregates @ 0.459 cum, machine mixed, concrete laid in layers not exceeing 15 cms thick, well compacted, in foundation, plinth and cills, including cost of all materials, labour, HOM of machinery, curing complete as per specifications, Specification No. KBS 4.1, 4.2 Page No. 13, Item No. 4.6 PWD SR 2018-19	Cum	34.22
6	Providing precast slab of 100 mm thick including cost of all materials, labour, curing including cost of all materials, labour, curing, Transportation, loading unloading, etc., complete as per the directin of engineer in charge - Data rate	Sqm	348.75
	Quantity above 125%	Sqm	103.05
7	Providing and fixing pre cast solid cement concrete kerb stones made out of CC 1:2:4 with top and bottom width 114 and 165 mm respectively, 400mm high and 450mm in length finished with CM 1:3. plastering and finishing cutting including formwork, curing, including cost of materials, labour charges of machinery, loading and unloading, lead and lift, transportation etc., complete Page No. 27 / Item No. 5.30 PWD SR 2018-19	No.	1613.00
8	KSRB 15-19.1 : Providing and applying ready mix priming cost over concrete / masonry / asbestos cement sheet / plastered surfaces including preparing the surface after thoroughtly cleaning of oil, grease, dirt and other foreign matter, and sand papering including cost of materials, labour complete as per specifications. Page No.124 / Item No. 15.80, PWD SR 2018-19	Sqm	326.70
9	KSRB 15-19.2 : Providing and applying spray painting in two coats (excluding priming coat) over concrete / masonry / asbestos cement sheet / plastered surfaces with flat wall paint of approved brant to give even shade after cleaning the surface of all dirt, dust and other foreign matter, and sand papering including cost of materials, labour complete as per specifications. Page No.124 / Item No. 15.81, PWD SR 2018-19	Sqm	326.70

Thanking you,

With Regards,

For Civil-Tech Consultants and Engineers

31/8/2019

Authorized Signature

Civil-Tech Consultants & Engineers Bangalore

Assistant Executive Engineer
Vidyaranyapura Sub Division
BBMP, Bangalore - 97

Improvements to Drains at Syndicate Bank road 5th Block BEL Layout in Ward No.09 (Vidyaranyapura), Vidyaranyapura Sub Division, BBMP, Bangalore.

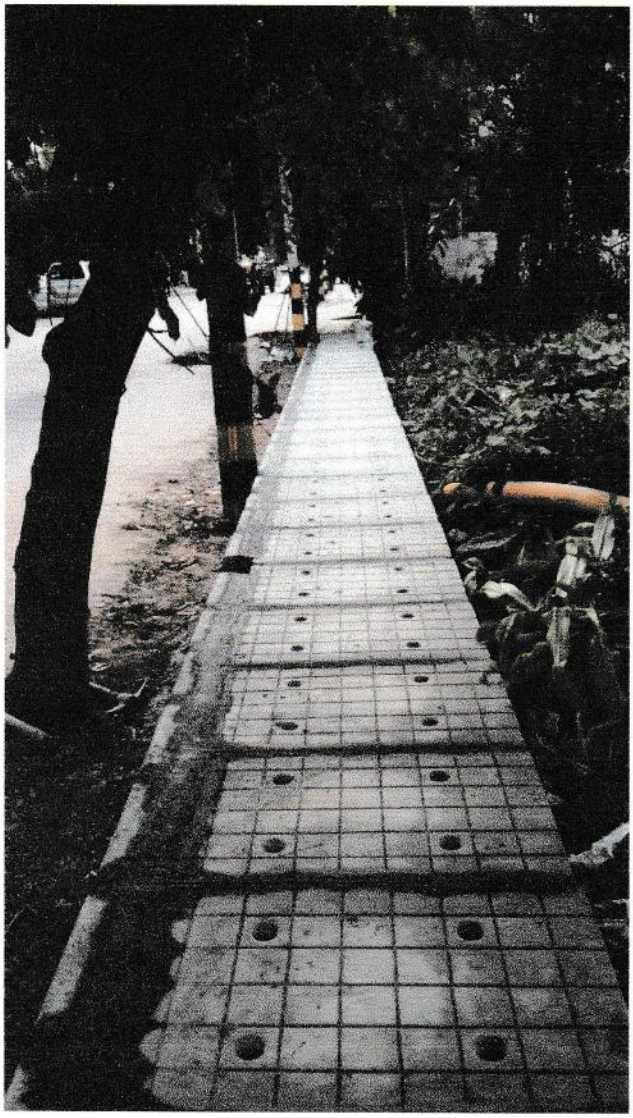

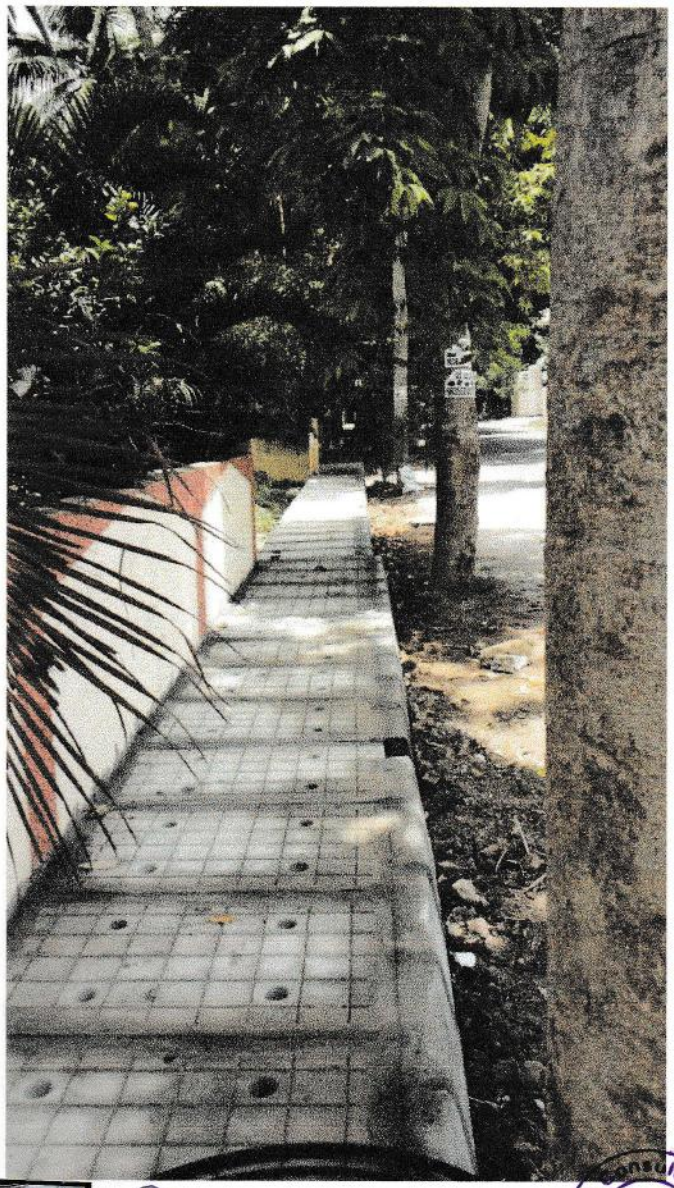

Assistant Executive Engineer
Vidyaranyapura Sub Division
BBMP, Bangalore - 97

Civil-Tech Consultants & Engineers * Bangalore

Improvements to Drains at Syndicate Bank road 5th Block BEL Layout in Ward No.09 (Vidyaranyapura), Vidyaranyapura Sub Division, BBMP, Bangalore.

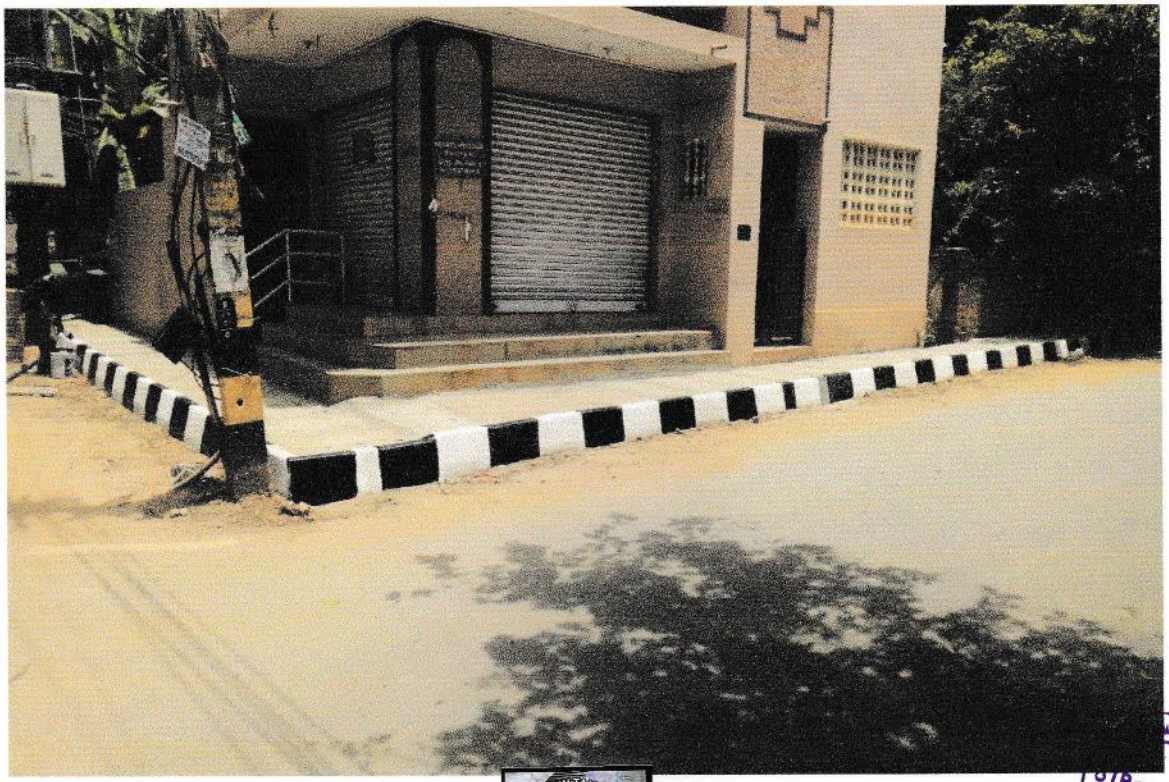

Assistant Executive Engineer
Vidyaranyapura Sub Division
BBMP, Bangalore
